

Construction Update

June 16, 2020

Numbers as available at the end of May 2020

Coastal GasLink

Construction highlights

With summer construction poised to begin, June has already seen a significant milestone on the Coastal GasLink route with the first pipe weld in the Kitimat area at the beginning of the month. This is the first of many thousands of pipe welds as mainline pipeline installation comes into focus for many sections along the route.

In early June, Aecon was named prime contractor for the Wilde Lake Compressor and Meter Station, and the Kitimat Meter Station. Compressor and meter facilities are important pieces of infrastructure that ensure natural gas is delivered safely and efficiently to LNG Canada's liquefaction facility in Kitimat.

Health and safety continue to be our primary focus. We are following Dr. Bonnie Henry's guidance and work with Northern Health as we progress construction activities through a measured and gradual ramp up of work over the coming weeks and months. Health and safety plans are in place across the project route, in accordance with guidelines issued by the BC Centre for Disease Control.

This includes having access to dedicated, 24/7 on-site medical services within lodges and worksites, reduced occupancy at all workforce sites, enhanced mandatory pre-screening, daily temperature checks, and symptomatic testing in consultation with Northern Health. You can learn more about the measures we're taking by visiting CoastalGasLink.com/Safety. Working together, we are confident that we can continue our important work across the project, while helping to protect the health and safety of our workforce, their families, and local communities.



Performance at a glance:



77%

of route cleared
**as estimated from field data at end of May*



358

workers at accommodation sites as of May 31

Under Construction

- ◆ Coastal GasLink Metering Facility
- ▲ Coastal GasLink Compression & Metering Facility

Potential Future Facilities

- ▲ Coastal GasLink Compression Facilities (TBD)
- LNG Canada Facility (3rd party)



1 Section 1: Monthly Construction Update

Performance at a glance:



86%
of route cleared



Chetwynd Lodge; Sanaata Lodge under development

Section 1


Location: West of Dawson Creek to south of Chetwynd

Length: 92 kilometres

Prime Contractor: Surerus Murphy Joint Venture

Workforce Accommodations: Two Workforce Accommodations – Chetwynd Lodge and Sanaata Lodge

- Project Right-of-Way (Section 1)
- Workforce Accommodation Site
- Storage Area (Where construction equipment and materials are stored)
- Kilometre Post Markings (KP)

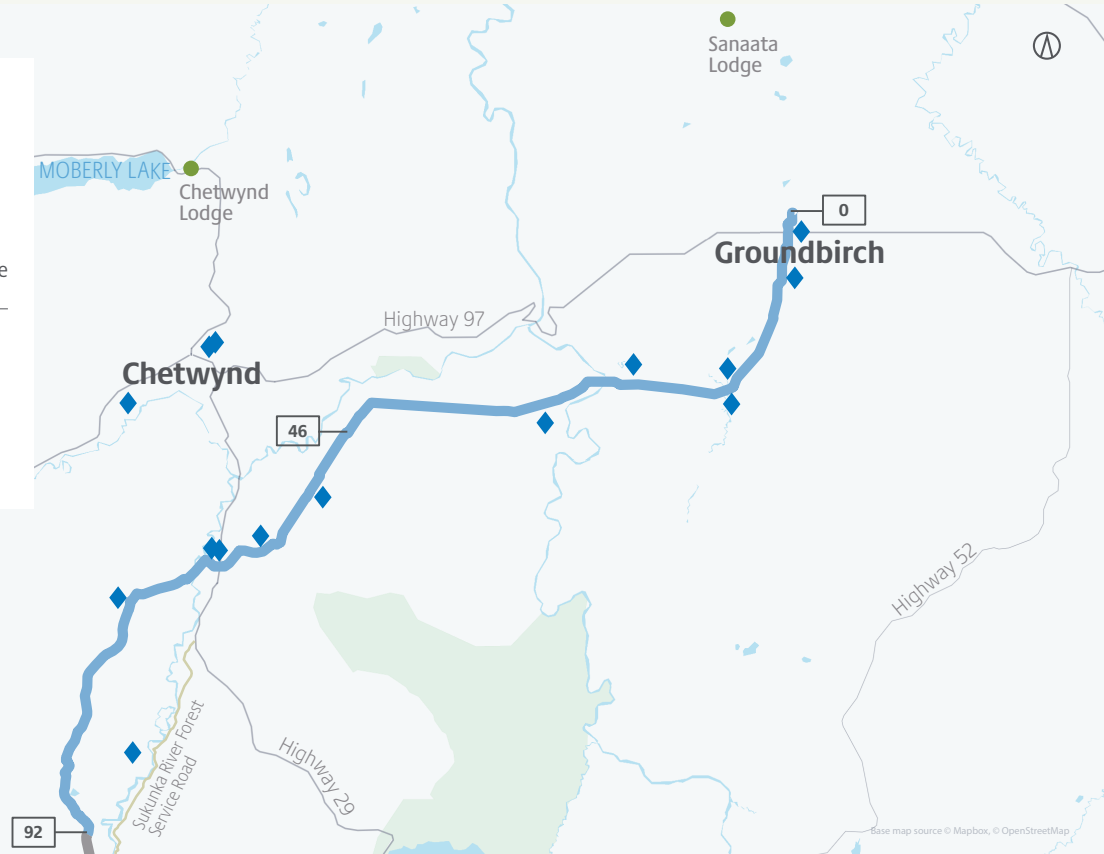

Construction progress:

- Completed pipe hauling and stockpiling pipe at section storage areas for this season; pipe hauling to resume in October 2020
- Aecon announced as prime contractor for Wilde Lake Compressor and Meter Station

Upcoming activities*:

- Finalizing construction readiness for summer mainline pipe installation
- Ongoing environment and erosion control monitoring and management
- Re-starting critical road upgrades, clearing works and grading in the Groundbirch area
- Resuming blasting as required from mid-June to end of August
- Drone surveys for environment and construction activities continue until end of the year
- Mainline pipeline construction in the Groundbirch area scheduled to commence mid-August

**All schedules are subject to change*

Did you know?

Sanaata Lodge will house workers constructing the Wilde Lake Compressor and Meter Station in the Groundbirch area. Visit Map.CoastalGasLink.com to view our interactive map and learn about each workforce accommodation site, including location and recent occupancy.

2 Section 2: Monthly Construction Update

Performance at a glance:



76%
of route cleared



0
workers at Sukunka Lodge

Section 2

Location: South of Chetwynd to east of McLeod Lake

Length: 48 kilometres

Prime Contractor: Surerus Murphy Joint Venture


Workforce Accommodations: Two Workforce Accommodations - Mt. Merrick Lodge and Sukunka Lodge

■ Project Right-of-Way (Section 2)

● Workforce Accommodation Site

◆ Storage Area (Where construction equipment and materials are stored)

□ Kilometre Post Markings (KP)

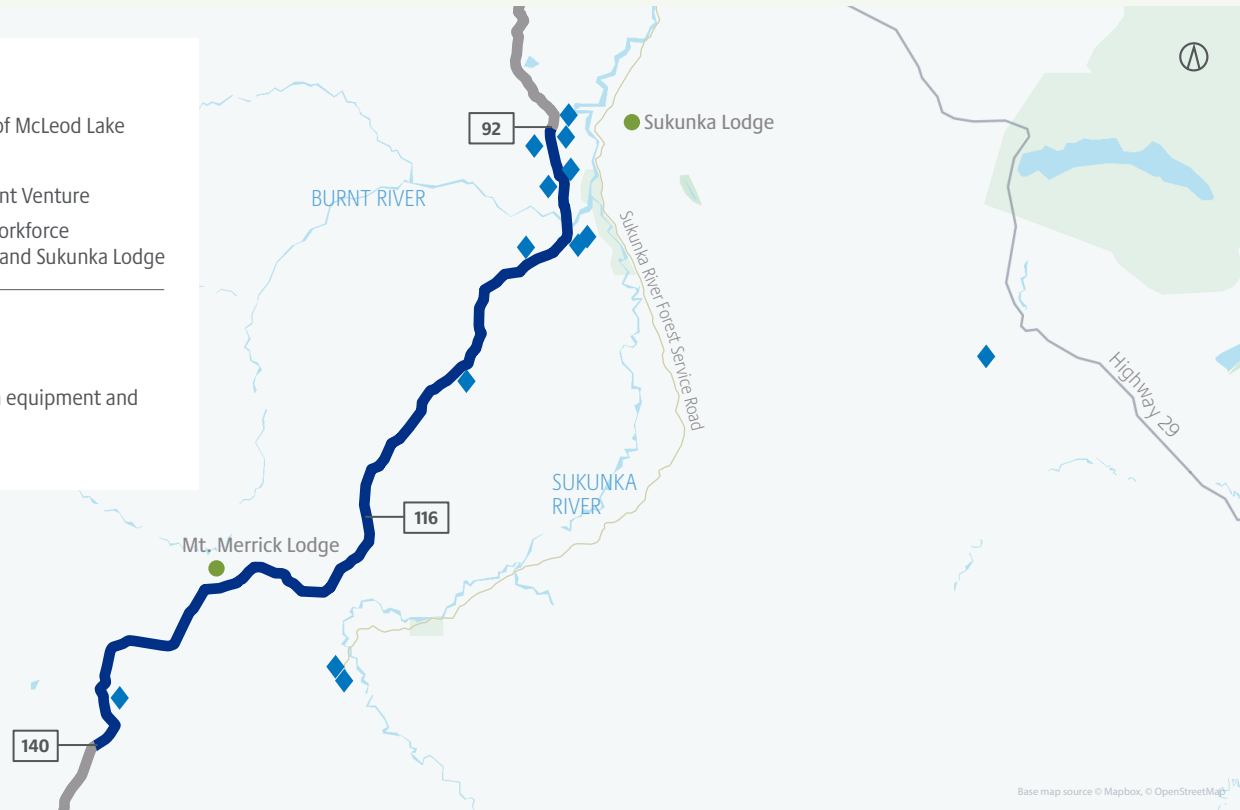

Construction progress:

- Road and bridge upgrades ongoing by road owners

Upcoming activities*:

- Preparing construction readiness for summer mainline pipe installation
- Ongoing environment and erosion control monitoring and management
- Anticipating re-start of critical road upgrades, clearing works and timber hauling in late June 2020, pending ground conditions
- Drone surveys for environment and construction activities continue until end of the year

**All schedules are subject to change*

3 Section 3: Monthly Construction Update

Performance at a glance:



77%
of route cleared



0
workers at Parsnip Lodge

Section 3

Location: East of McLeod Lake to north of Prince George

Length: 104 kilometres

Prime Contractor: SA Energy Group

Workforce Accommodations: One Workforce Accommodation – Parsnip Lodge

— Project Right-of-Way (Section 3)

● Workforce Accommodation Site

◆ Storage Area (Where construction equipment and materials are stored)

□ Kilometre Post Markings (KP)



Construction progress:

- Hand falling of trees along the route as required

Upcoming activities*:

- Ongoing environment and erosion control management
- Preparing construction readiness for summer mainline pipe installation
- Drone surveys for environment and construction activities continue until end of the year
- Pipe deliveries continue to storage areas until April 2021

**All schedules are subject to change*

Did you know?

Hand falling — or cutting — trees requires careful planning and highly skilled professionals. It's a time-intensive clearing technique for larger trees but is used as an important method to ensure safety.

4 Section 4: Monthly Construction Update


Performance at a glance:



98%
of route cleared



Vanderhoof Lodge under development

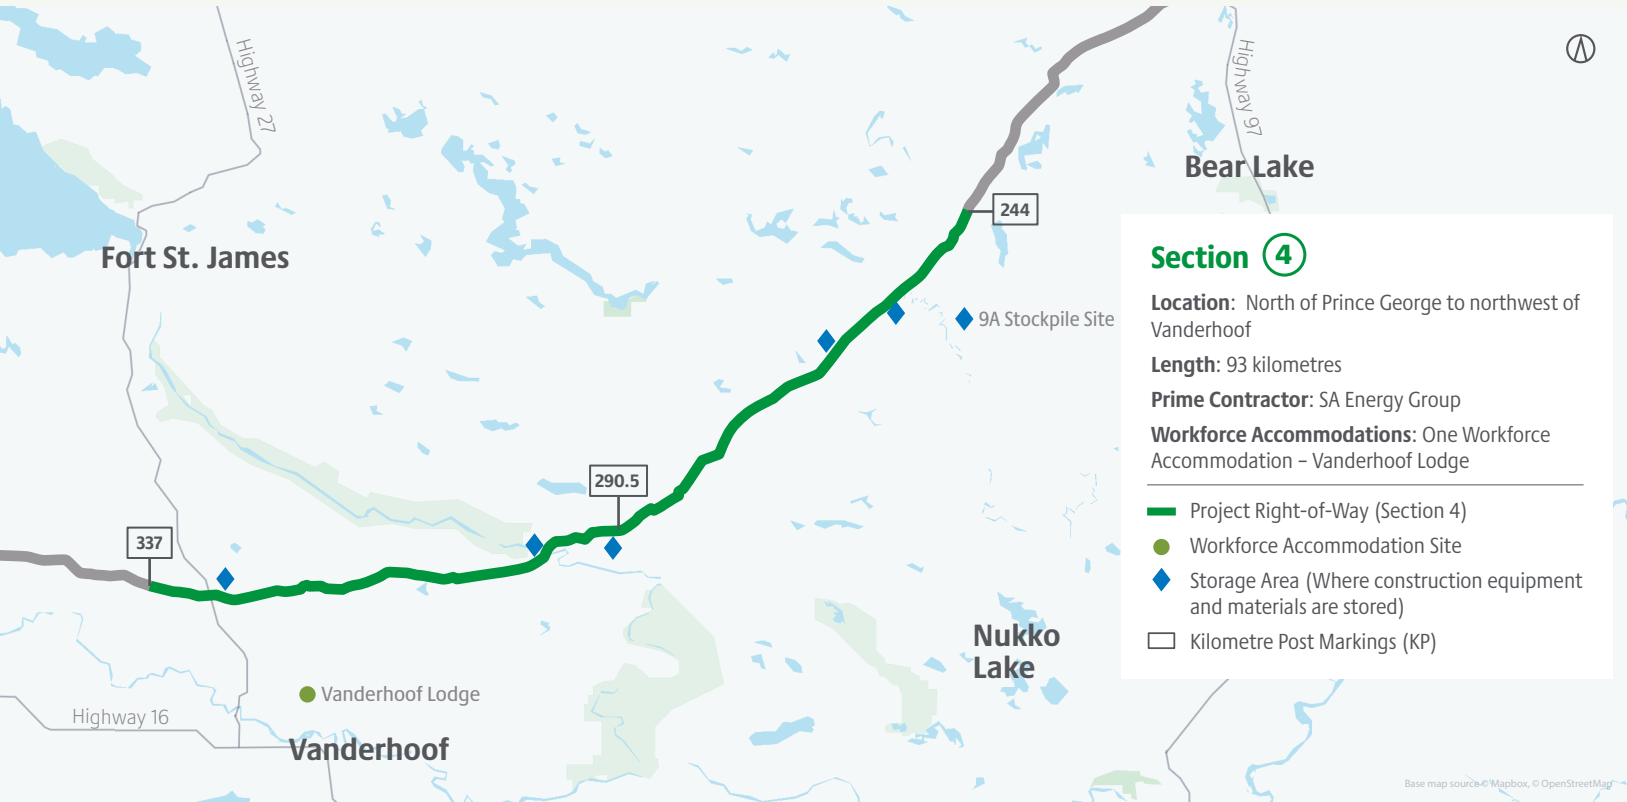

Construction progress:

- Vanderhoof Lodge construction ongoing
- Stuart River bridge deck landed safely on the piers on the opposite side
- Restoration and clean-up of 9A storage site

Upcoming activities*:

- Continue construction of Vanderhoof Lodge, with first occupancy expected in mid-June
- Stuart River bridge construction activities; anticipated bridge opening in late June
- Begin access road construction in mid-June
- Complete construction readiness reviews for summer mainline pipe installation
- Drone surveys for environment and construction activities continue until end of the year

**All schedules are subject to change*

5 Section 5: Monthly Construction Update

Performance at a glance:



100%
of route cleared



48
workers at Little Rock Lake Lodge

Section 5

Location: North of Vanderhoof to south of Burns Lake

Length: 82 kilometres

Prime Contractor: Macro Spiecapag Joint Venture (MSJV)

Workforce Accommodations: One Workforce Accommodation – Little Rock Lake Lodge

— Project Right-of-Way (Section 5)

● Workforce Accommodation Site

◆ Storage Area (Where construction equipment and materials are stored)

□ Kilometre Post Markings (KP)



Construction progress:

- Ongoing erosion and sediment control monitoring
- Ongoing site and access preparation at section storage areas

Upcoming activities*:

- Preparing construction readiness for summer mainline pipe installation
- Ongoing erosion and sediment control
- Drone surveys for environment and construction activities continue until end of the year

**All schedules are subject to change*

6 Section 6: Monthly Construction Update

Performance at a glance:



97%
of route cleared



113
workers at 7 Mile Road Lodge



Construction progress:

- Ongoing erosion and sediment control
- Ongoing site preparation at 7 Mile Road Lodge site and section storage areas

Upcoming activities*:

- Begin right-of-way grubbing and construction access construction and upgrades
- Receive pipe at Section 6 storage areas
- Begin construction at borrow sites, including blasting
- Preparing construction readiness for summer mainline pipe installation
- Blasting activities continuing as required by right-of-way conditions
- Drone surveys for environment and construction activities continue until end of the year

**All schedules are subject to change*

7 Section 7: Monthly Construction Update

Performance at a glance:



0%
of route cleared



Huckleberry Lodge site
under development

Section 7

Location: South of Houston to north of Morice Lake

Length: 78 kilometres

Prime Contractor: Pacific Atlantic Pipeline Construction Inc. (PAPC)

Workforce Accommodations: One Workforce Accommodation – Huckleberry Lodge

- Project Right-of-Way (Section 7)
- Workforce Accommodation Site
- Storage Area (Where construction equipment and materials are stored)
- Kilometre Post Markings (KP)



Construction progress:

- Commenced civil works for Huckleberry Lodge and associated access

Upcoming activities*:

- Preparing construction readiness for summer clearing and construction
- Pipe to arrive at Section 7 storage sites until April 2021
- Blasting activities continuing as required by ancillary site conditions
- Drone surveys for environment and construction activities continue until end of the year
- Development of first phase of the Huckleberry Workforce Accommodation site and access

**All schedules are subject to change*

8 Section 8: Monthly Construction Update

Performance at a glance:



78%
of route cleared



197
workers at Sitka Lodge and Hunter Creek Lodge

Section 8


Location: North of Morice Lake to Kitimat

Length: 84 kilometres

Prime Contractor: Macro Spiecapag Joint Venture (MSJV)

Workforce Accommodations: Seven Workforce Accommodations – Sitka Lodge, Hunter Creek Lodge, Icy 1 Lodge, Icy 2 Lodge, P2 Lodge, 9A Lodge, P4 Lodge

- Project Right-of-Way (Section 8)
- Workforce Accommodation Site
- ◆ Storage Area (Where construction equipment and materials are stored)
- Kilometre Post Markings (KP)

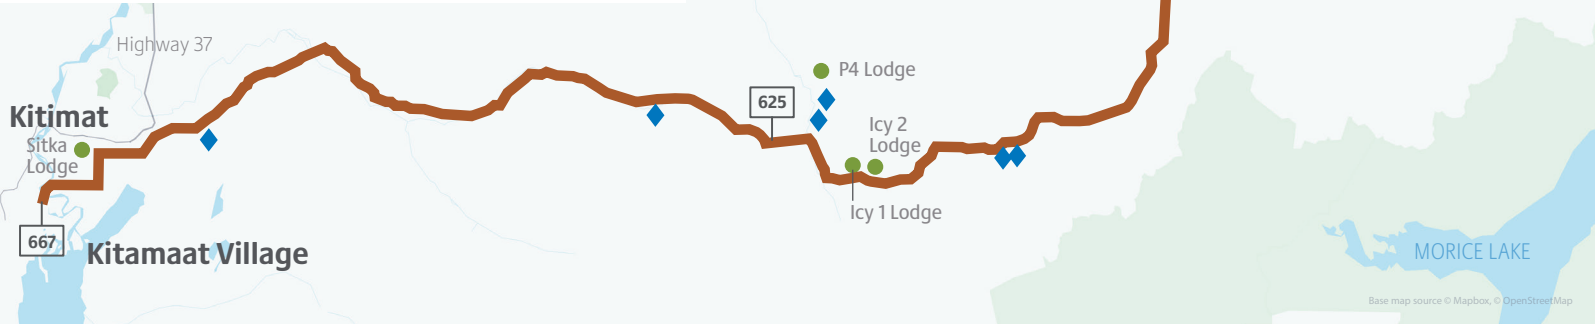

Construction progress:

- Continued road and bridge works in the Kitimat Valley, District of Kitimat and North Hirsch areas
- Commenced civil works for 9A Lodge as part of renovating this facility
- Hunter Creek workforce accommodation operational

Upcoming activities*:

- Ongoing site preparation at Kitimat River for under river pipe installation
- Continue clearing on priority work fronts
- Blasting activities continuing as required by right-of-way conditions
- General maintenance on North Kitimat, North Hirsch, South Hirsch and Shea roads
- Continue work at Hunter Creek and 9A Lodges
- Preparing construction readiness for summer mainline pipe installation
- Pipe deliveries continue in the Kitimat area until April 2021
- Drone surveys for environment and construction activities continue until end of the year

**All schedules are subject to change*



Photo of the month Aerial view of Section 7 pipe yard

Pipes are stored and organized in preparation for installation at a pipe yard near Houston.



About Coastal GasLink's Construction Updates

Our construction updates include information on recent progress, activities that we expect over the next month and detailed section maps, that help communicate where project infrastructure is located and where activities are happening.

Check us out!

Find information, such as Construction Updates and an interactive map, on CoastalGasLink.com.

Keep in touch and learn more

We want to make sure you have access to the information you need about the project. Here are the many ways you can reach out, and learn more:



Visit our website:
CoastalGasLink.com



Follow us on Facebook:
[@CoastalGasLink](https://www.facebook.com/CoastalGasLink)



Sign up to receive our Connector Newsletter: CoastalGasLink.com/contact



Email us:
coastalgaslink@tcenergy.com



Follow us on Twitter:
[@CoastalGasLink](https://www.twitter.com/CoastalGasLink)



Visit our community office:
Prince George
760 Kinsmen Place

Coastal GasLink

