

NOVEMBER 2014 HIGHLIGHTS



DREDGING
Completed



WATER TREATED
Completed



CAPPING
140,000 cubic yards of capping material placed.



HABITAT / PLANTS / WETLANDS
7,500 plants, shrubs, and trees planted.

Onondaga Lake Cleanup Progress

NOVEMBER 1 – NOVEMBER 30, 2014

Onondaga Lake dredging, capping, and habitat enhancement continue under the supervision of the New York State Department of Environmental Conservation (DEC), the U.S. Environmental Protection Agency (EPA), and the New York State Department of Health (DOH).

Major Projects	Progress in November 2014	Project Total	% Complete To Date
Barrier Wall	Complete	1.5 miles	100%
Pipeline	Complete	3.9 miles	100%
Water Treatment Plants	Complete	3 plants	100%
LCP Chemicals Cleanup Site	Complete	7 tons of mercury removed	100%
Lake Material Removed	Complete	2 million cubic yards*	100%
Cap Material Placed	140,000 cubic yards	2.8 million cubic yards*	60%
Water Treated	Complete	2.8 – 3.1 billion gallons*	100%
Wetlands Improved	3 acres	50 acres*	80%
Plants, Shrubs, Trees Planted**	7,500 plants	1.1 million*	29%

*Estimated totals

**Does not include 400,000 shrub willows

Onondaga Lake Dredging and Capping Progress


LEGEND 2012/2013/2014

- Dredging in Progress
- Dredging Complete
- Dredge Areas



LEGEND 2012/2013/2014

- Capping in Progress
- Capping Complete
- Cap Areas

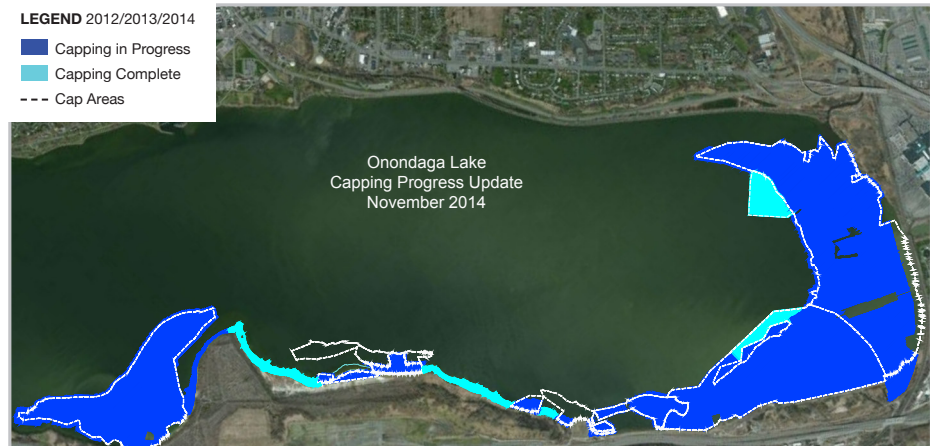

Honeywell

For more information, please contact Honeywell at 315.552.9784, or visit www.lakecleanup.com.
